

Chronology of Field Operations and Adjustments

Presentation to the National Academy of Sciences, Engineering, and Medicine's Panel to Evaluate the Quality of the 2020 Census

August 31, 2021

Albert E. Fontenot, Jr., Associate Director Decennial Census Programs

*All estimates are considered preliminary. Final counts and percentages will be released as part of the 2020 Census Operational Assessments series.

Shape
your future
START HERE >

United States[®]
Census
2020


2020 Census

Operational Timelines

Activity / Operation	Original Dates	Operational Adjustments Due to COVID-19	Replan Dates	Final Dates
Self-Response Phase	March 12 – July 31	March 12 – October 31	March 12 – October 15*	March 12 – October 15
Update Leave (Stateside)	March 15 – April 17	June 13 – July 9	Phased re-opening occurred between May 4 and June 12	Phased re-opening occurred between May 4 and June 12
Service Based Enumeration	March 30 – April 1	Needs further review and coordination with outside partners and stakeholders	September 22 – 24	September 22 – 24
Targeted Non-Sheltered Outdoor Locations	March 31 – April 1	Needs further review and coordination with outside partners and stakeholders	September 23 – 24	September 23 – 24
Group Quarters Enumeration	April 2 – June 5	July 1 – September 3	April 2 – September 3	April 2 – September 3
Enumeration of Transitory Locations	April 9 – May 4	Tentatively September 3 – September 28, but may need further review and coordination	September 3 – 28	September 3 – 28
Nonresponse Followup	May 13 – July 31	August 11 – October 31	August 9 – October 15*	August 9 – October 15
Delivery of Apportionment Data	By Statutory Deadline: December 31, 2020	Deliver by April 30, 2021	As close to statutory deadline as possible	April 26, 2021
Delivery Redistricting Data	By Statutory Deadline: March 30, 2021	Deliver by July 31, 2021	As close to statutory deadline as possible	August 12, 2021


* From Sept. 28 – Oct. 2, 2020, end date was Oct. 5, 2020

2020 Census Operational Timelines

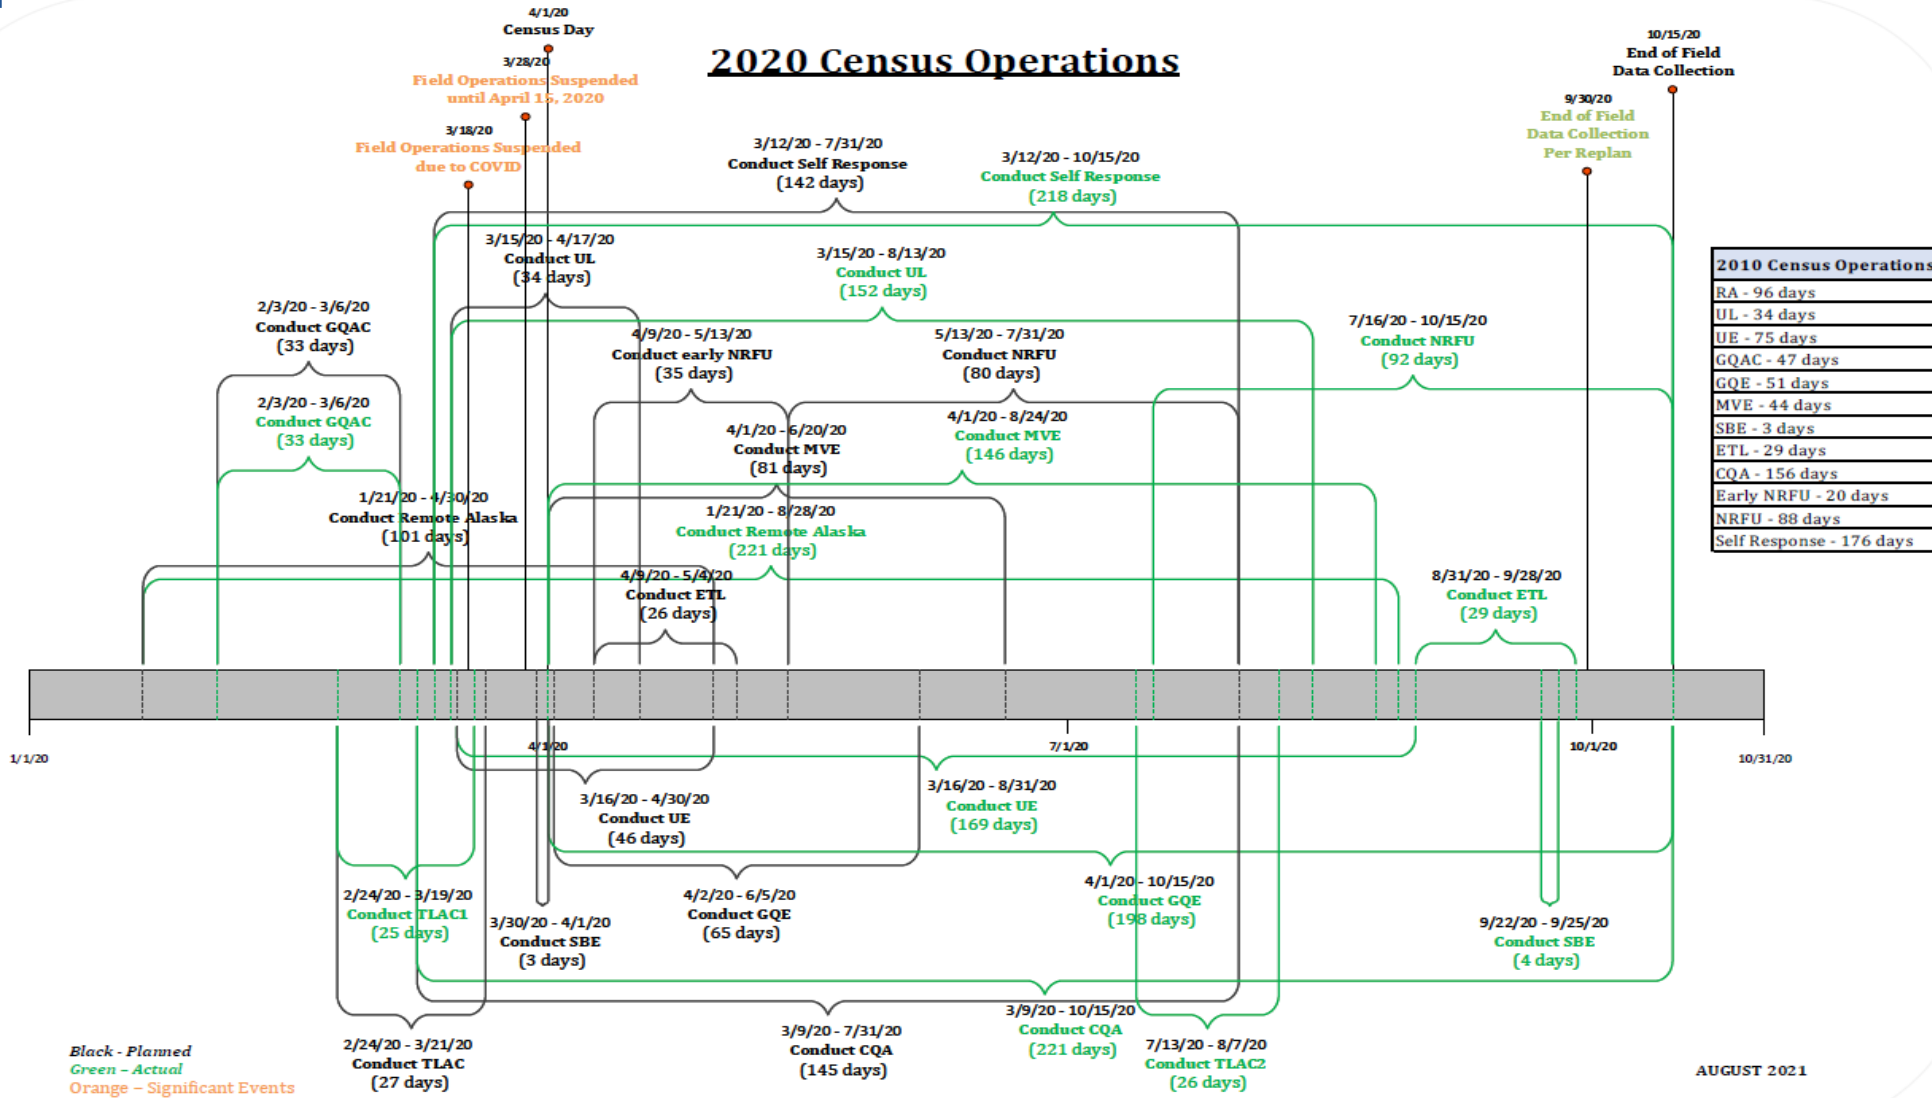


2020 Census Operational Timelines

2020 Census Remote Alaska Operation

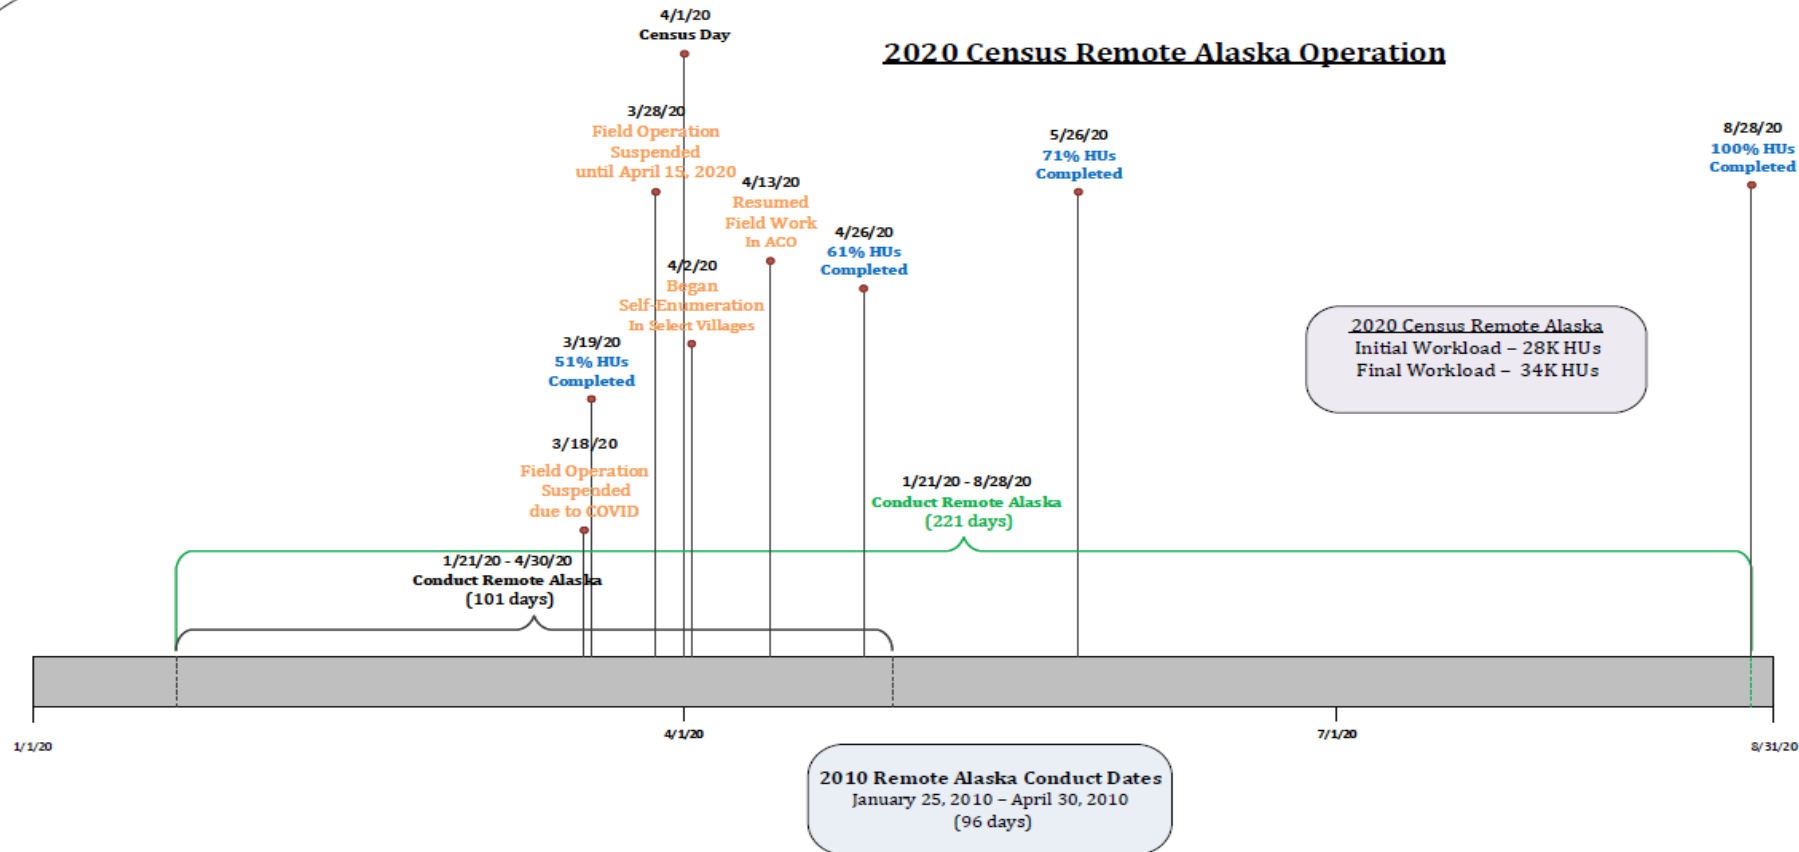

AUGUST 2021


2020 Census Operational Timelines

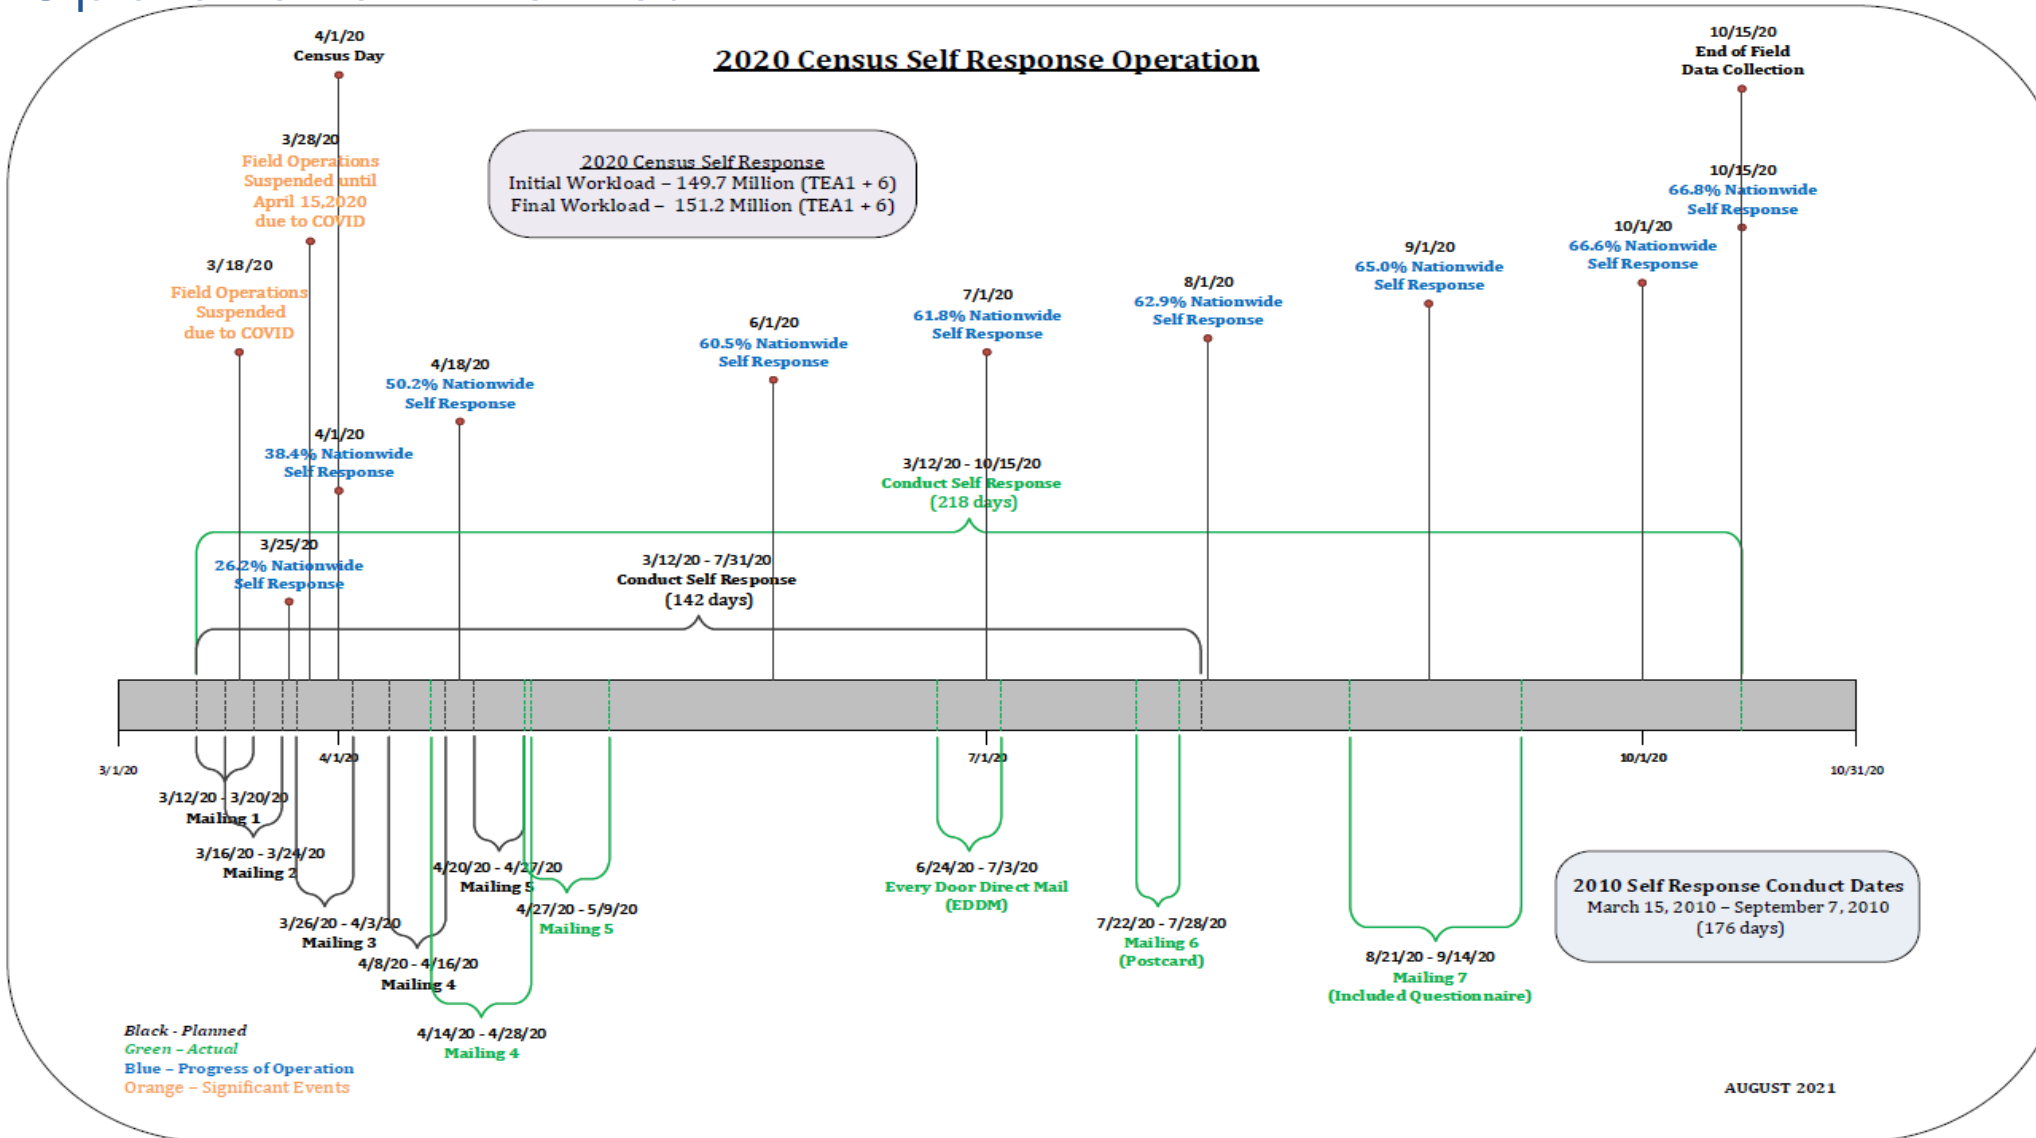

2020 Census

Operational Timelines

2020 Census CQA Operation

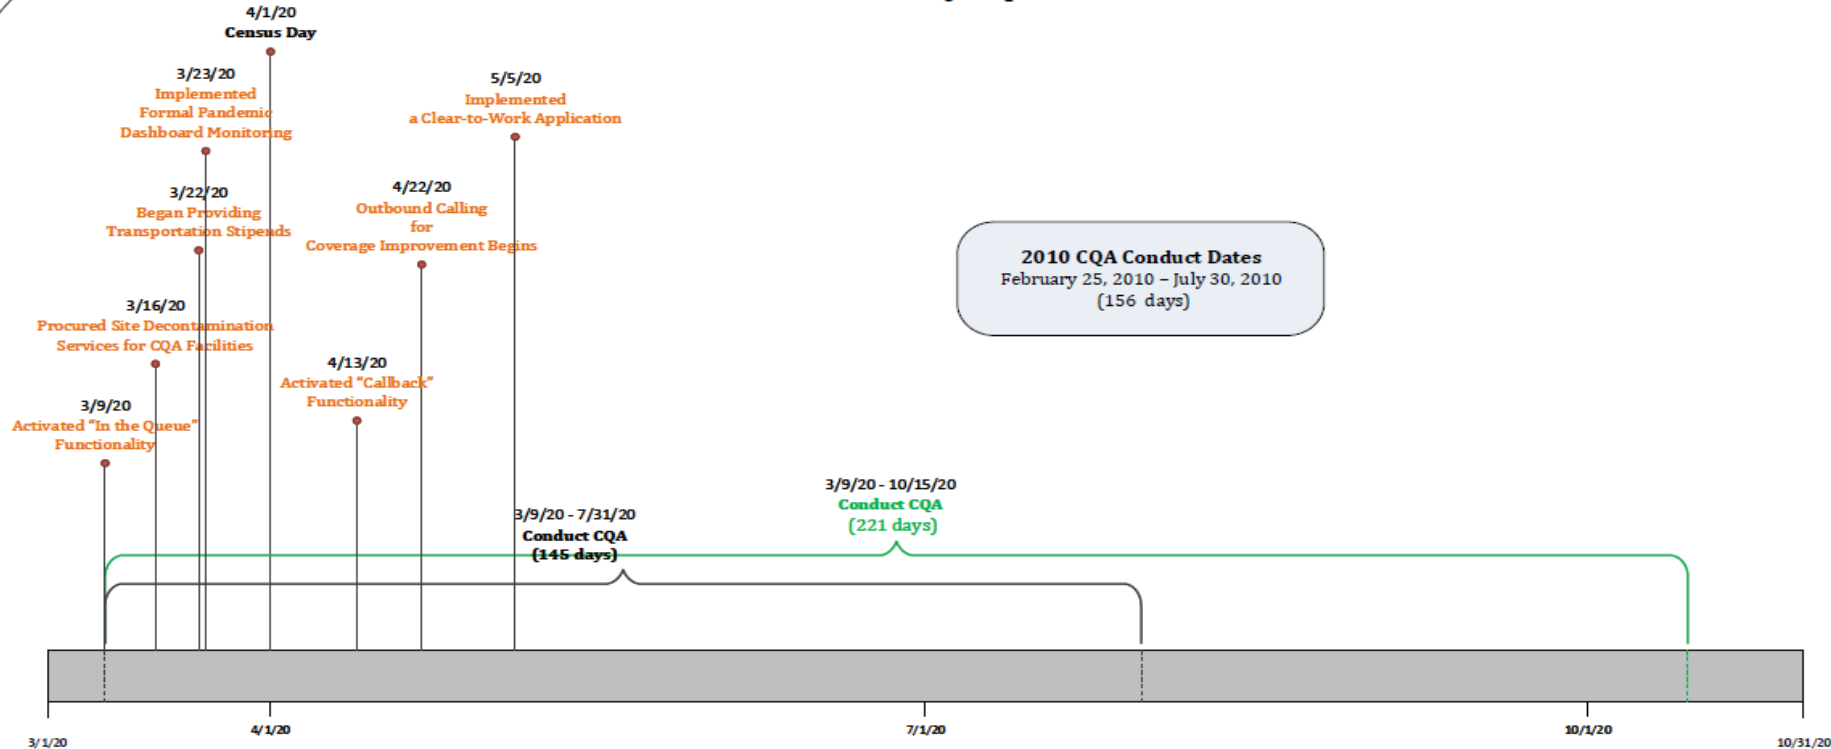


Black - Planned
Green - Actual
Orange - Significant Events

AUGUST 2021

2020 Census Operational Timelines

2020 Census UL Operation

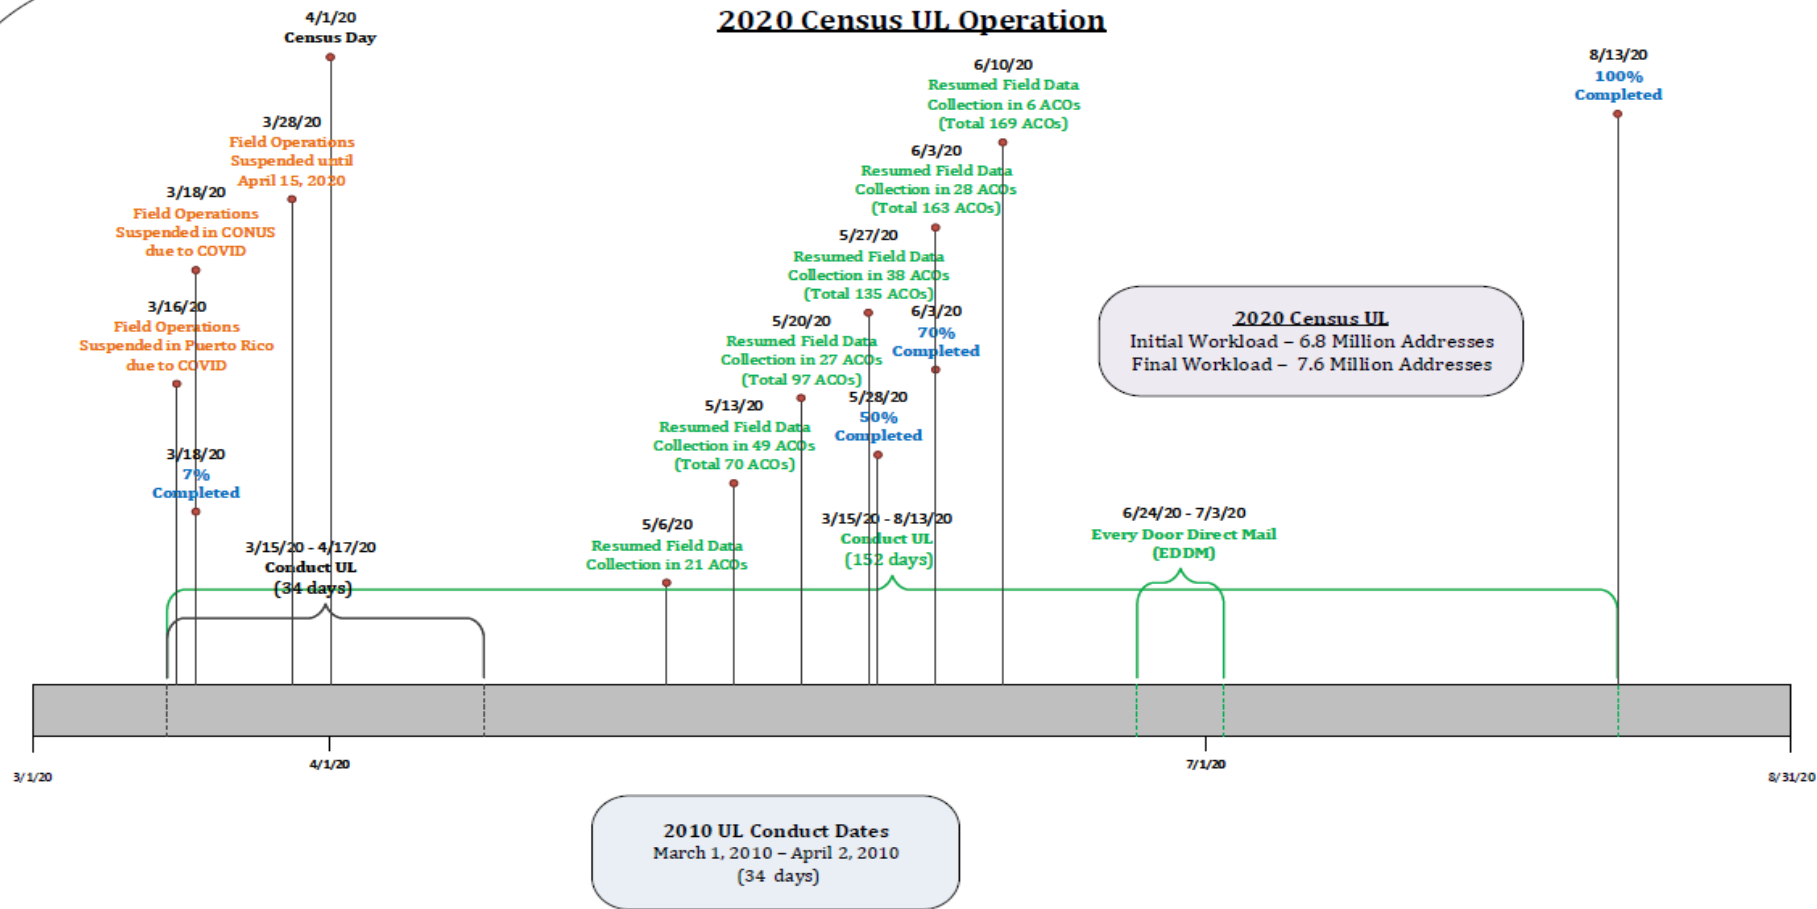


Black - Planned
Green - Actual
Blue - Progress of Operation
Orange - Significant Events

AUGUST 2021

2020 Census Operational Timelines

2020 Census UE Operation

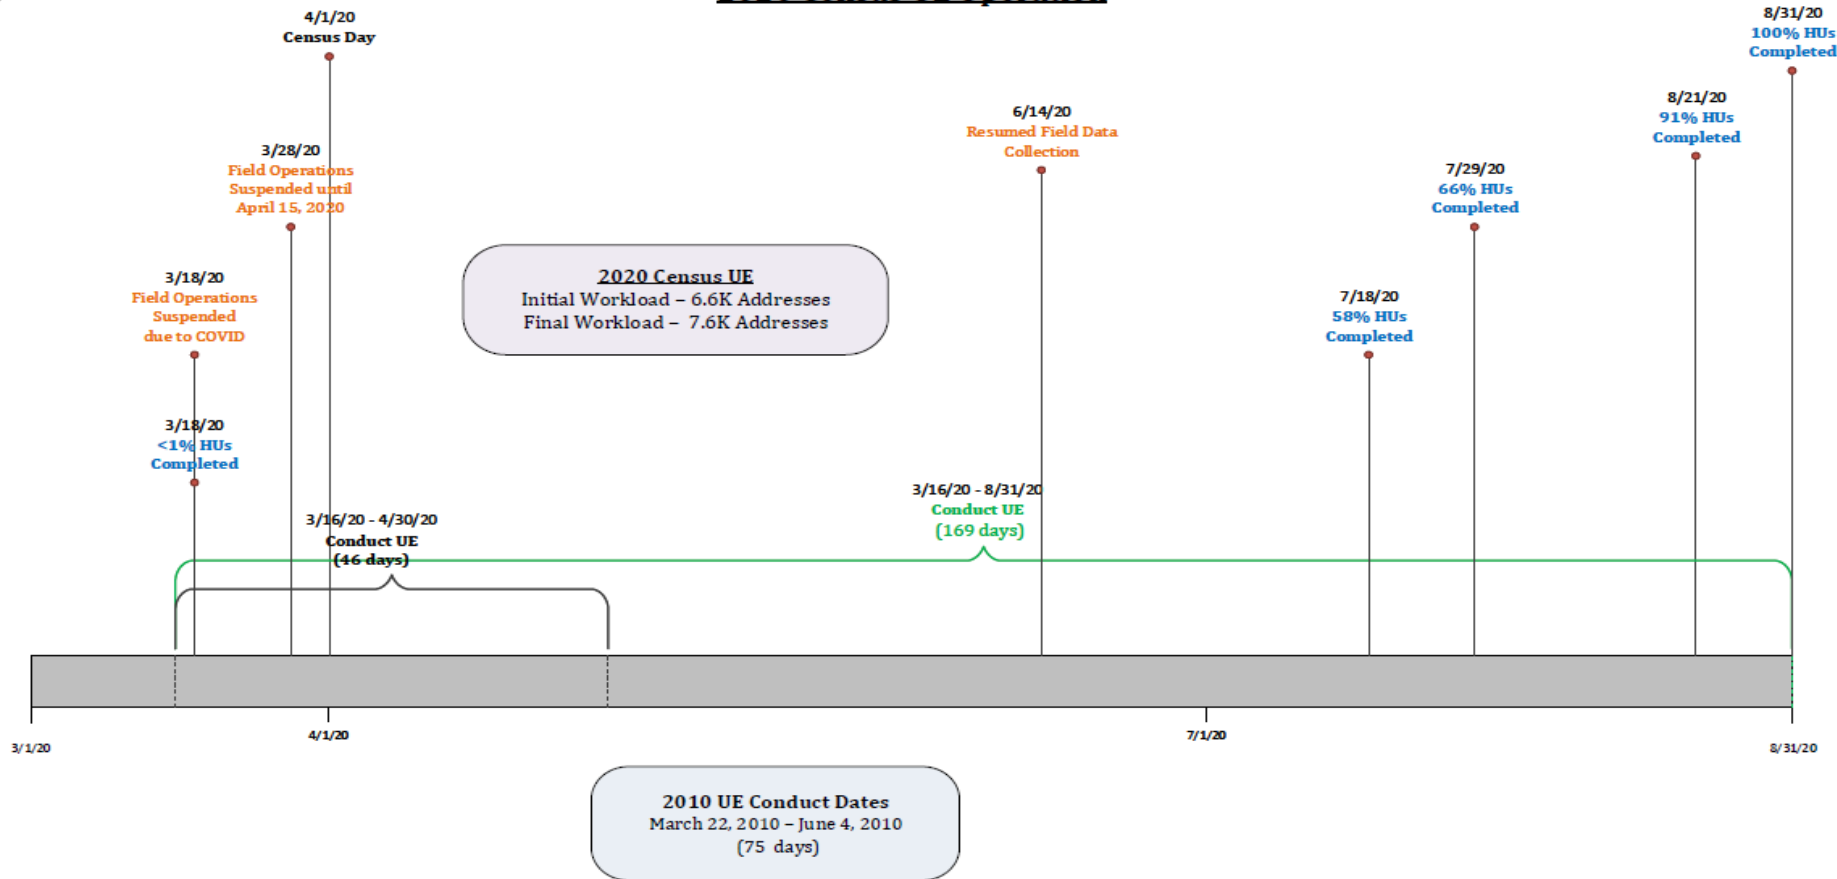


Black - Planned
Green - Actual
Blue - Progress of Operation
Orange - Significant Events

AUGUST 2021

2020 Census Operational Timelines

2020 Census GQAC Operation

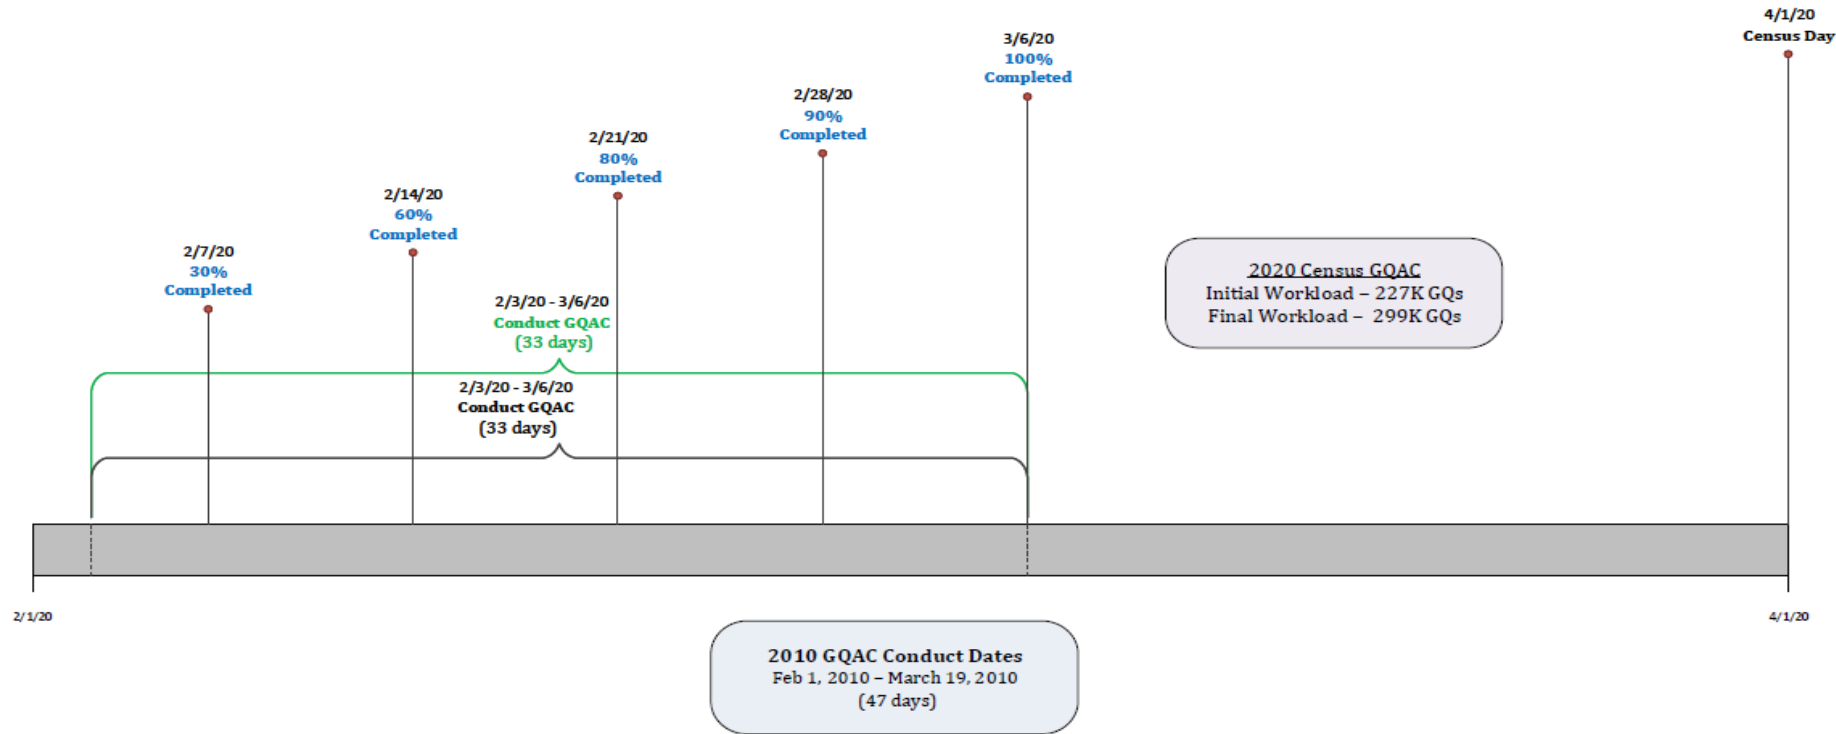


AUGUST 2021

2020 Census

Operational Timelines

2020 Census GQE Operation

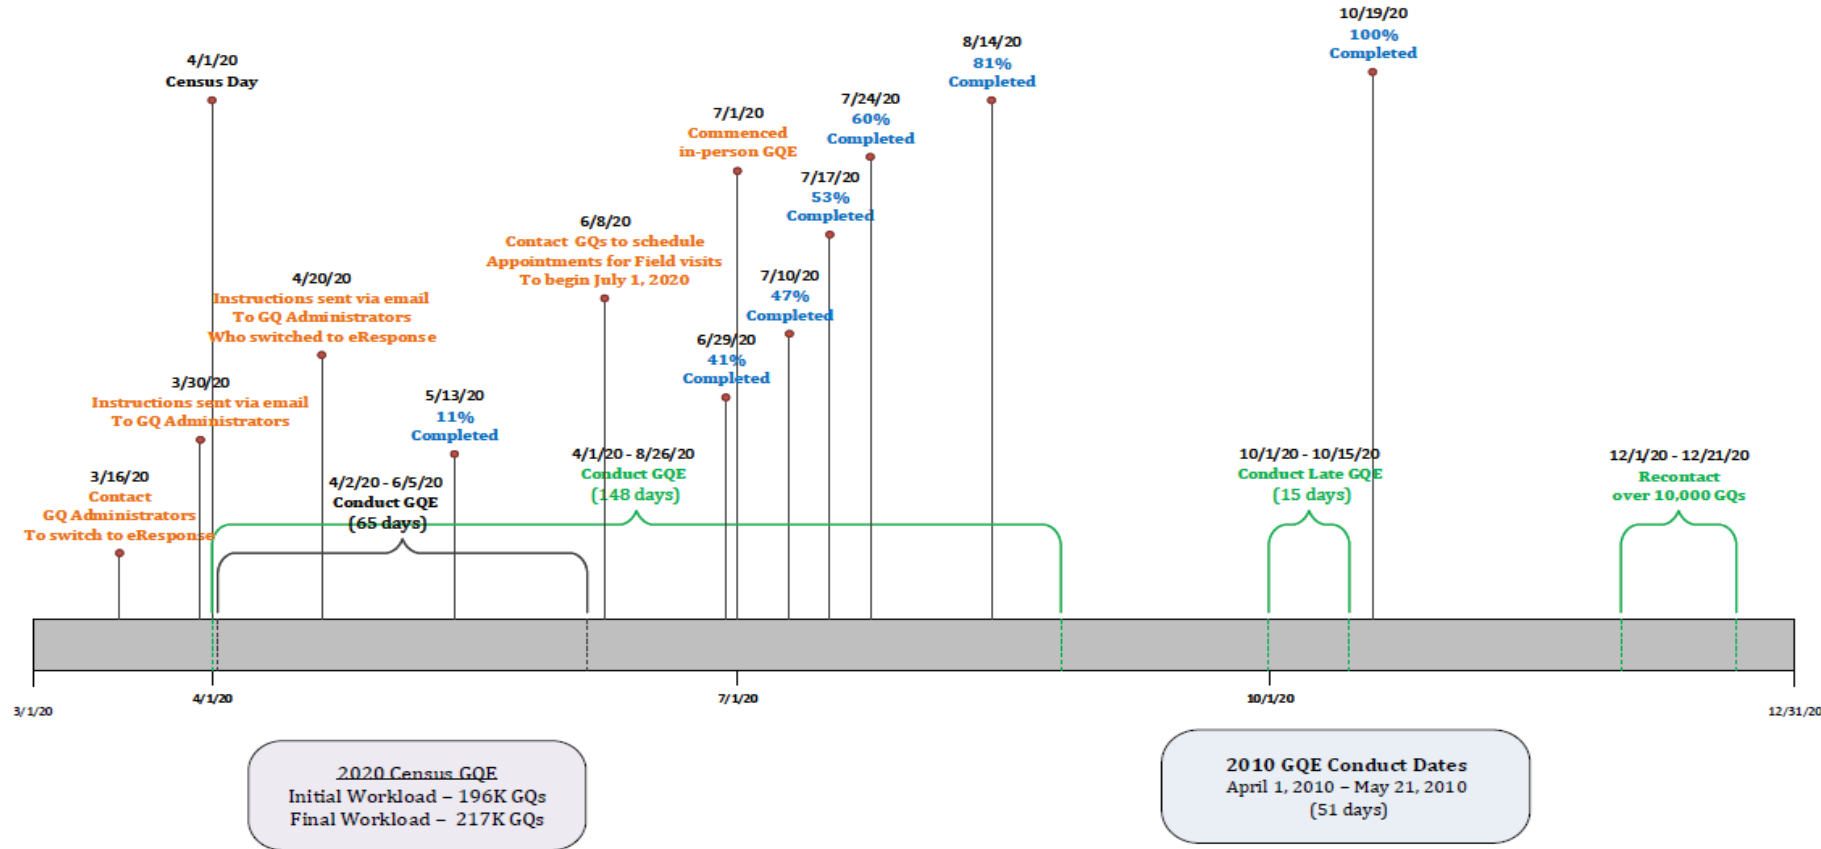


Black - Planned
Green - Actual
Blue - Progress of Operation
Orange - Significant Events

AUGUST 2021

2020 Census

Operational Timelines

2020 Census MVE Operation

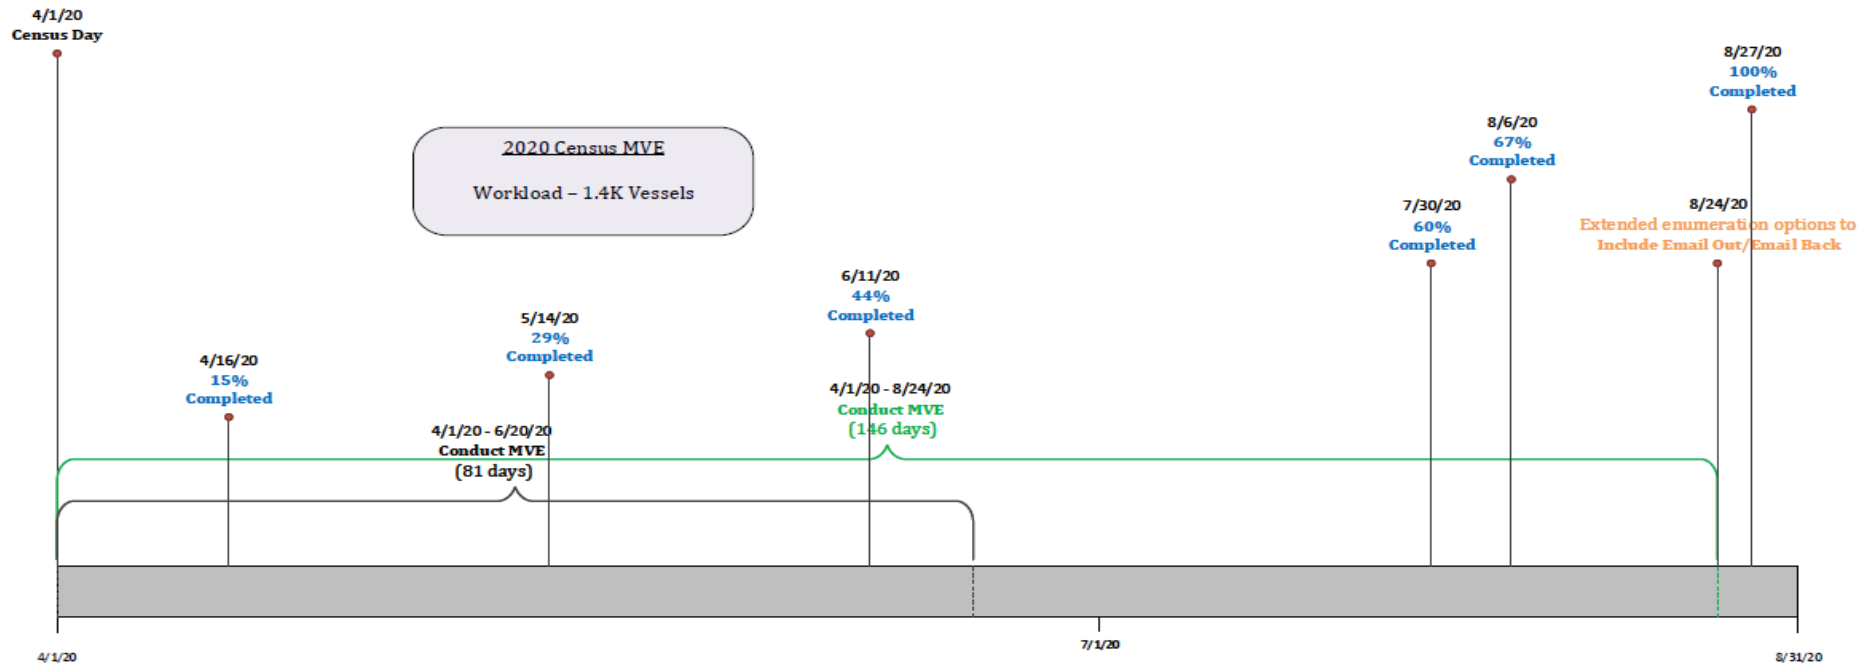


AUGUST 2021

2020 Census

Operational Timelines

2020 Census SBE Operation

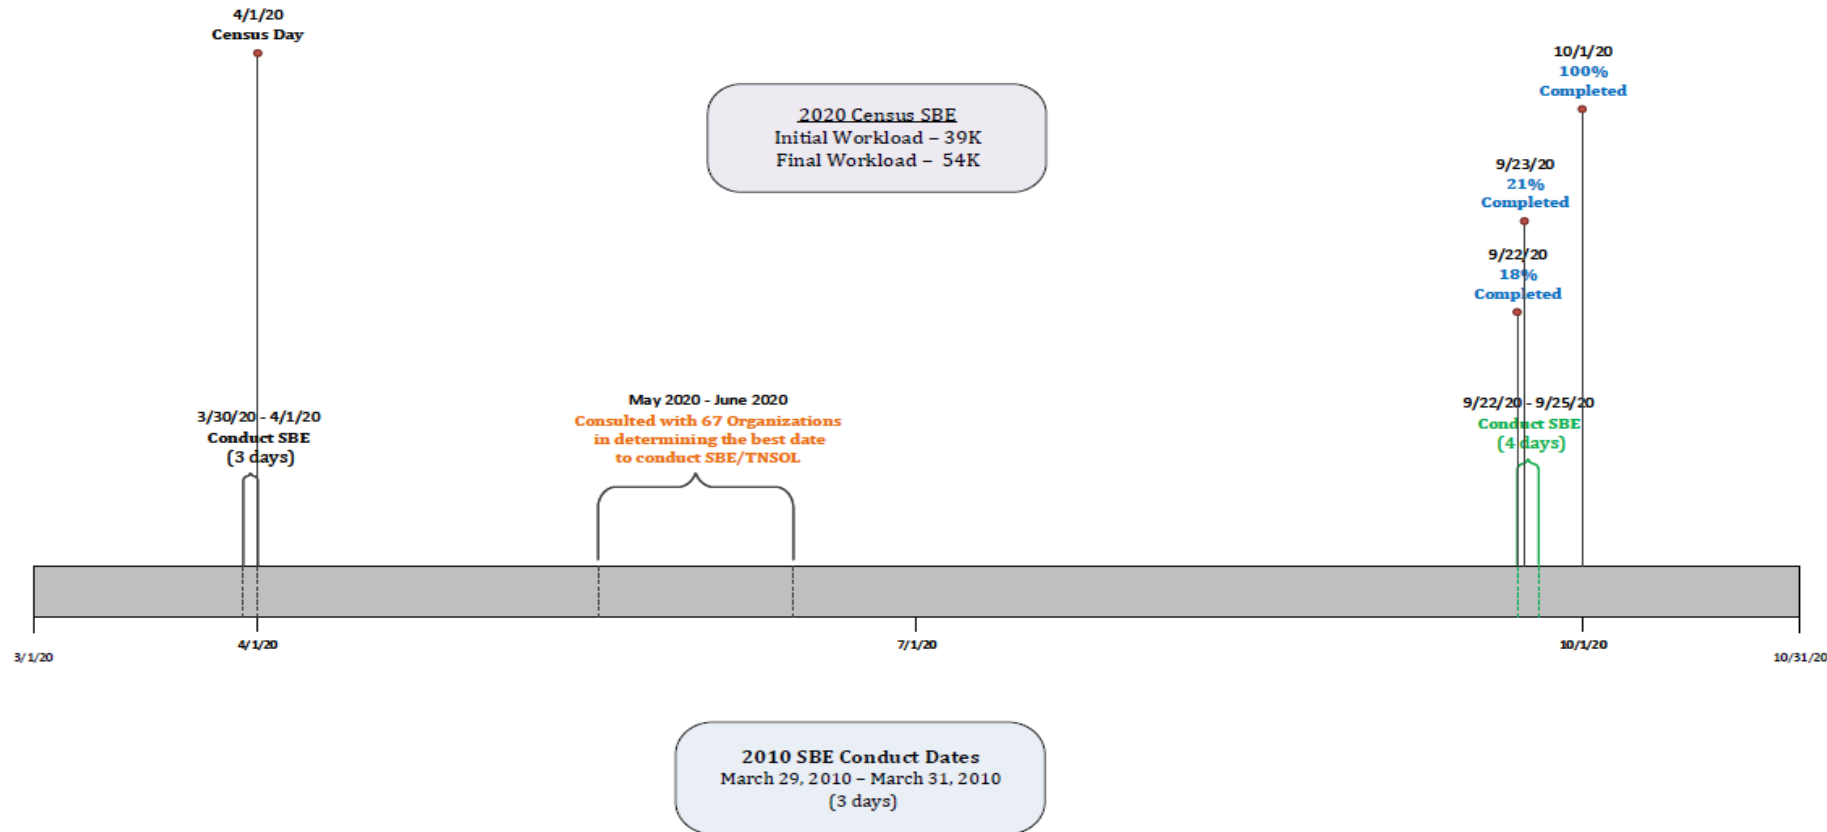


Black - Planned
Green - Actual
Blue - Progress of Operation
Orange - Significant Events

AUGUST 2021

2020 Census Operational Timelines


2020 Census TLAC Operation

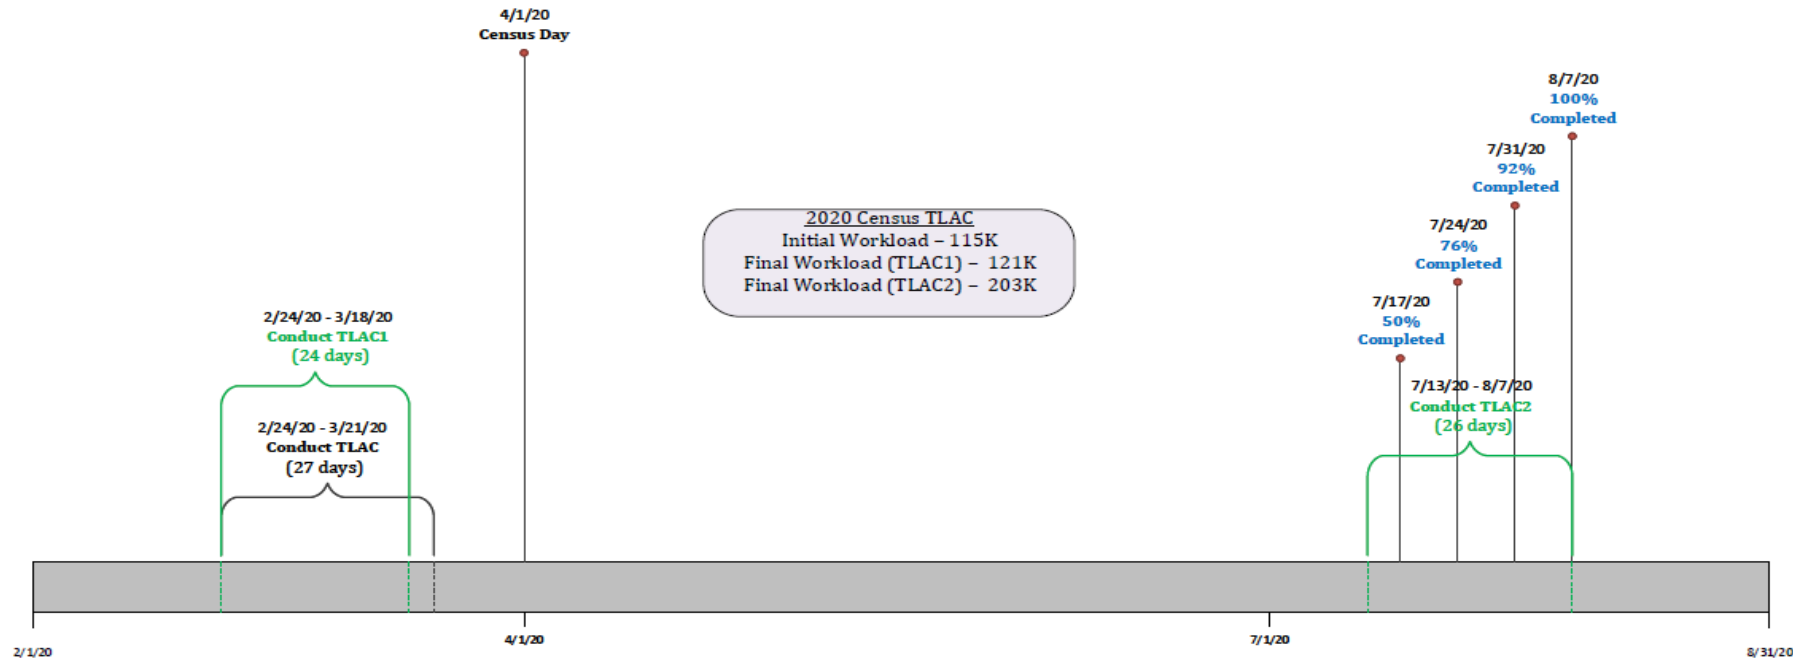

AUGUST 2021

2020 Census Operational Timelines


2020 Census ETL Operation

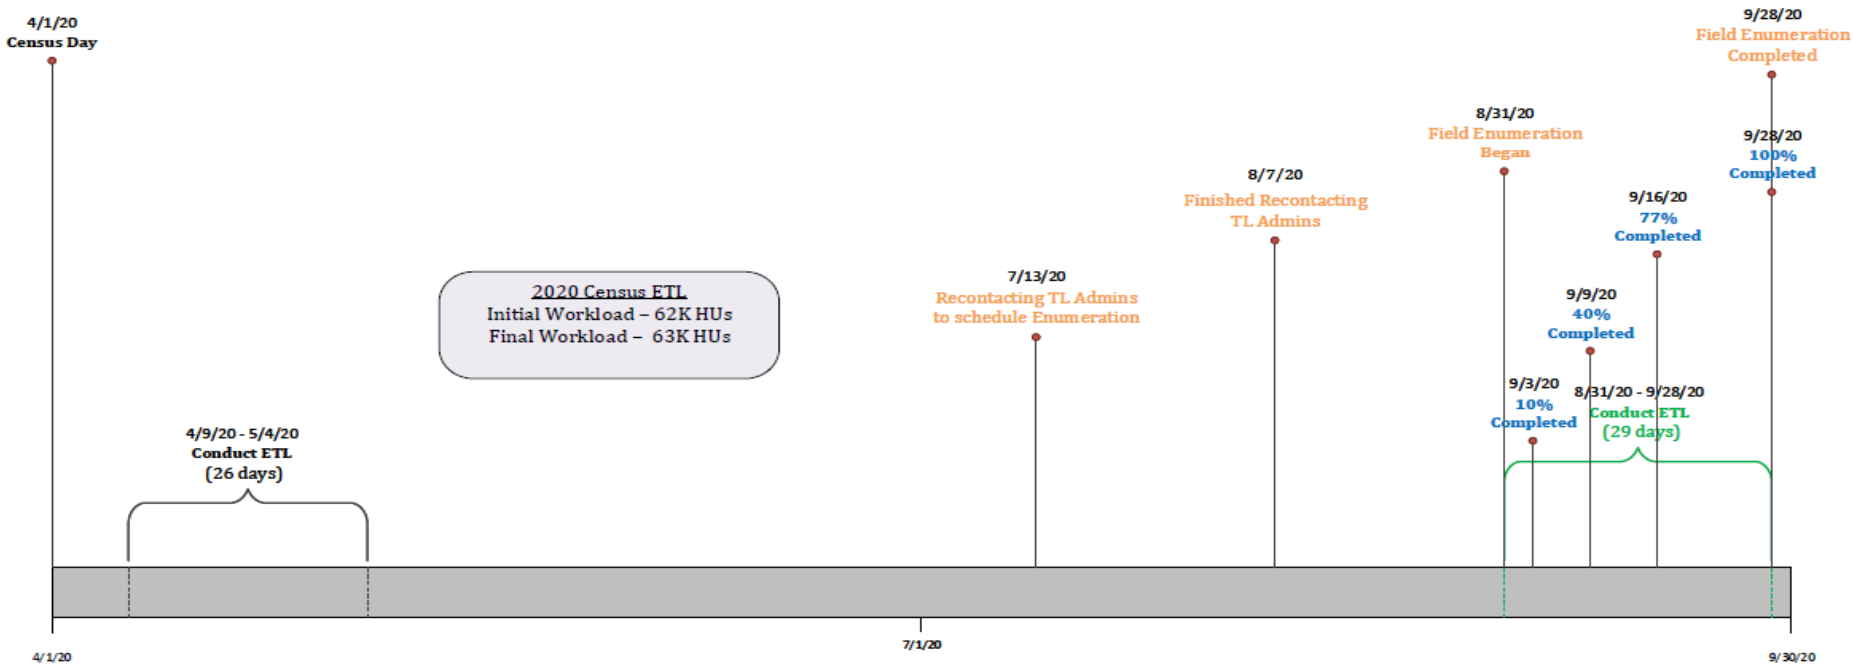

Black - Planned
Green - Actual
Blue - Progress of Operation
Orange - Significant Events

AUGUST 2021

2020 Census Operational Timelines

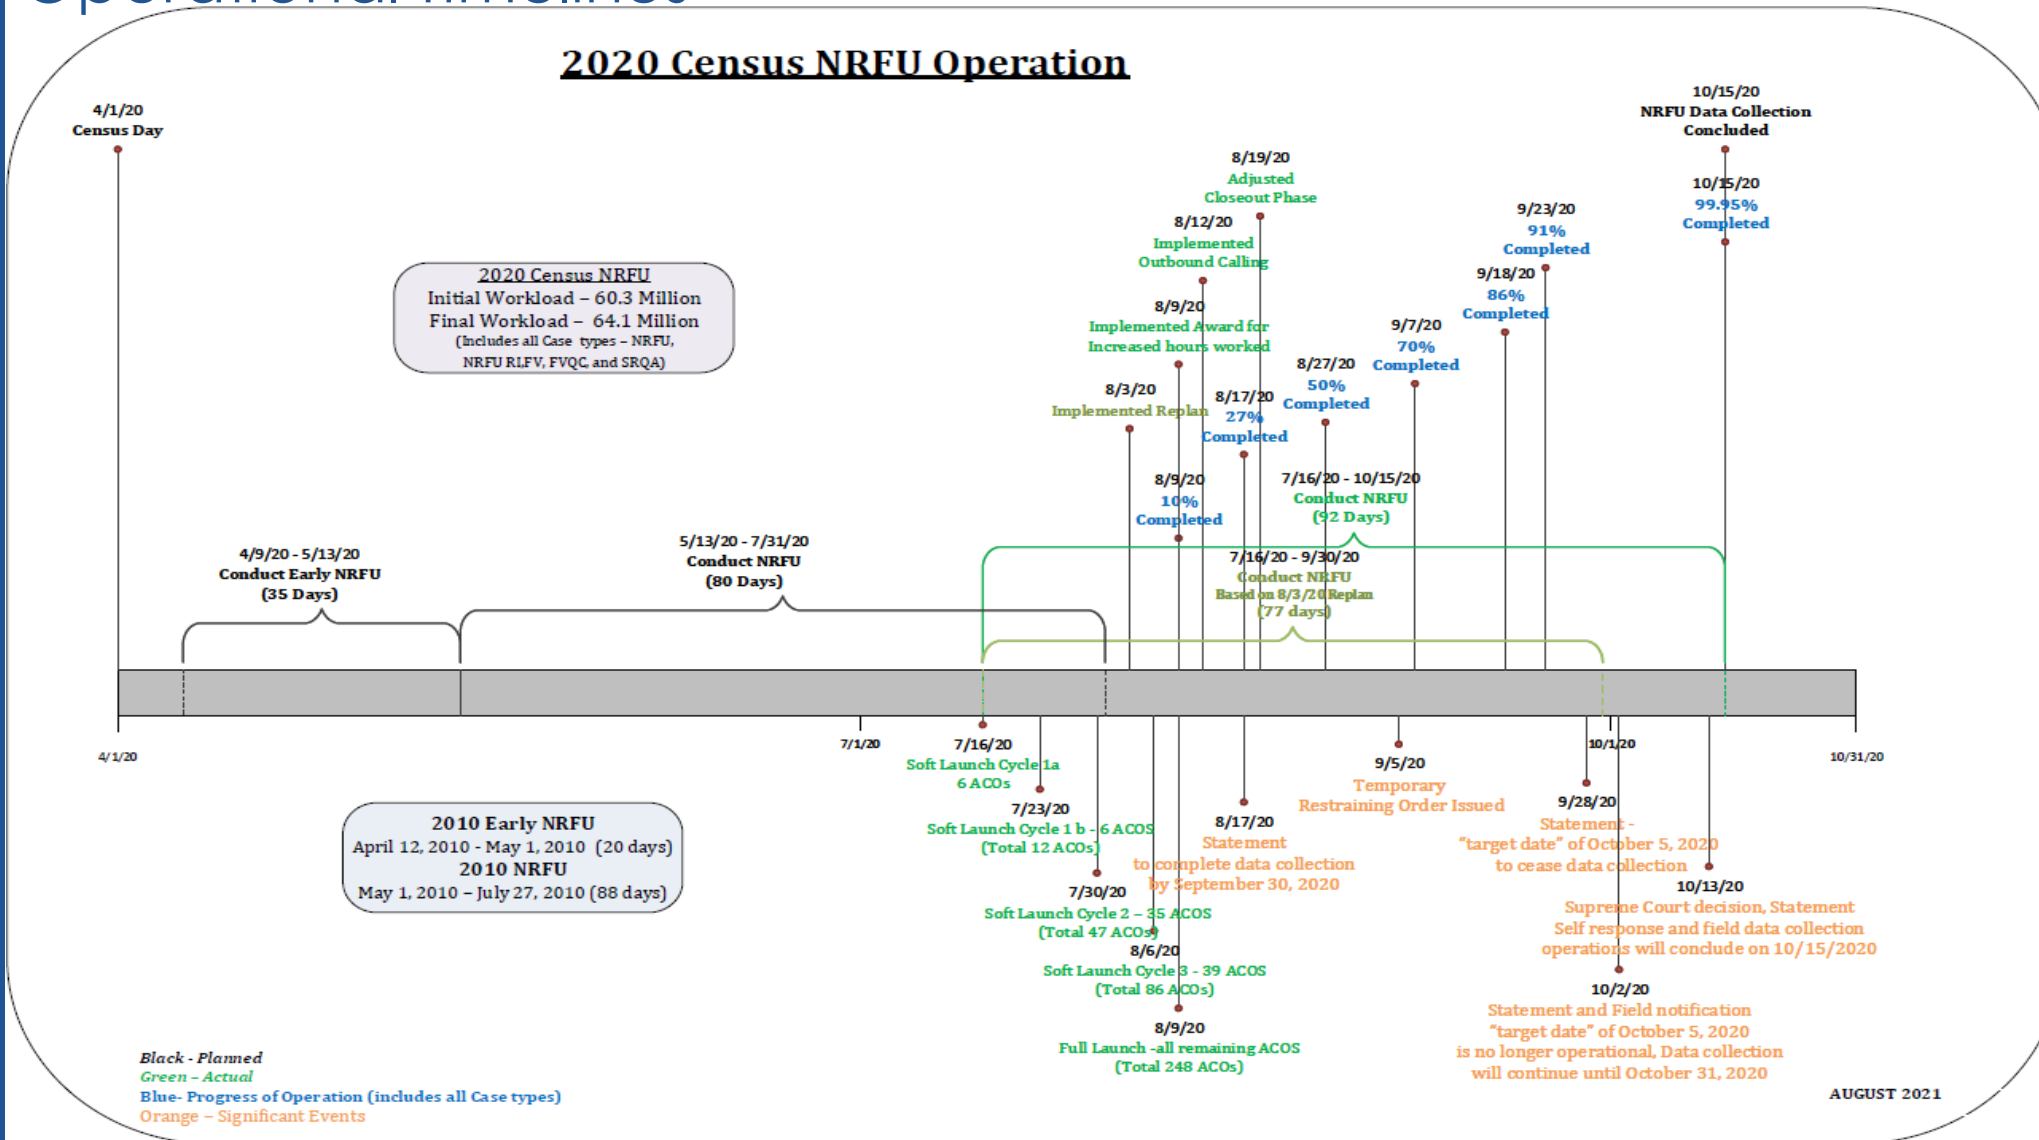

2020 Census

Planned and Actual Processing Schedule

Processing Step	Planned Dates	Actual Dates
Decennial Response File 1 (DRF1)	September 15, 2020 – October 15	October 29, 2020 – December 26
Decennial Response File 2 (DRF2)	October 16 – November 7	December 26 – February 24, 2021
Census Unedited File (CUF)	November 8 – December 5	February 25 – March 10
Apportionment Preparation and Release	December 6 – December 27	March 12 – April 26
Census Edited File (CEF)	November 25 – January 26, 2021	April 20 – June 24
Disclosure Avoidance Application/Microdata Detail File	January 26 – February 10	June 25 – July 18
Tabulation File Processing	February 10 – March 19	July 19 – August 12
Redistricting Preparation and Release	February 17 – March 31	August 13 – September 30

Questions
